Project Name : PharmaLink

Project Sponsor : National Pharmaceutical Association

Project Manager : Maria Ayman

Purpose of the Project : Connect all pharmacies in a central network to help users quickly find and locate medicines .

Business Case : This application saves time, reduces stress, and increases access to medications, especially for urgent or less-common drugs. Pharmacies can attract more customers by being discoverable through the app, while healthcare agencies gain better insight into local medicine availability.

Key Deliverables

- Fully functional mobile app (Android and iOS)

Project Milestones Timeline

Milestone	Description	Deadline
Planning	Define scope, goals, timeline, and responsibilities.	31/10/2025
Hardware, Network & Licenses	Prepare needed devices, connectivity, and licenses for the project.	31/01/2026
Development	Finalize mobile UI/UX , backend structure ,Coding, system integrationfirst full app build	20/02/2026
Quality Control	QA testing, bug fixing, user feedback	14/03/2026
Release	Launch in app stores, pharmacy staff onboarding	22/03/2026
Advertisement & Marketing	Promote the product to target users.	01/04/2026

Resources

- **Staff**: 2 Flutter developer , 1 back-end developer, 1 content specialist, 1 QA/tester
- **Hardware**: 5 laptops, 1 Server , 5 mobile devices
- **Software/Tools**: Software **licenses (IDE , database , mapping APIs)**

Budget Estimate : Total Estimated Budget is **450,000 EGP**

Constraints

- Must deliver within the budget and timeline specified
- High data quality required for real-time medicine updates from pharmacies
- Pharmacy registration for credibility
- Required legal approvals for health data

High Level Risks

- Delays in onboarding pharmacies or integrating their inventory systems
- Technology compatibility issues with legacy pharmacy databases
- App user adoption and possible training required for pharmacy staff
- Unforeseen infrastructure or medication availability issues
- Data privacy, especially regarding health and prescription information

Project Scope Statement

1. Product Scope Description

The PharmaLink application is a mobile platform designed to connect all pharmacies within a central network, empowering users to quickly locate and access medicines. The app includes:

- Real-time search for medication availability at local pharmacies.
- Location-based maps showing pharmacy locations and stock levels.
- Pharmacy registration and verification features for credibility.
- Pharmacy contact and directions interface.
- Multi-language support (Arabic and English).
- Android and iOS compatibility.
- Live chat support with pharmacists.

The purpose is to reduce wait times, enhance treatment access, and streamline pharmacy discovery for users in urgent or routine situations.

2. Product Acceptance Criteria

The project will be accepted if:

- The app functions smoothly on Android and iOS devices.
- Users can easily search and find available medicines.
- Pharmacies are able to update inventory in real time.
- The interface is user-friendly and meets accessibility standards.
- Legal and privacy requirements for health data are fulfilled.
- App is approved by the sponsor after user testing.

3. Project Deliverables

- Fully developed and tested **PharmaLink App** (Android + iOS).
- Backend server and pharmacy inventory management database.
- **User documentation** (User guide and FAQs).
- **Project documentation** (requirements, design, test reports).
- Pharmacy staff onboarding materials and training guides.
- **Deployment package** and maintenance plan.
- Post-launch marketing or app store promotion.

4. Project Exclusions

The following items are ***not* included** in this scope:


- Web-based version of the application (mobile only).
- Integration with insurance or third-party delivery services.
- Handling payment transactions through the app.

5. Project Constraints

- Total budget limited to **450,000 EGP**.
- Project must be completed by **01/04/2026.**
- Only registered and validated pharmacies may participate.
- Limited development resources (2 Flutter devs, 1 backend, 1 content, 1 QA).
- Must comply with health data protection and privacy regulations.

6. Project Assumptions


- National Pharmaceutical Association will provide up-to-date pharmacy data.
- Developers will have access to all necessary development tools.
- Pharmacies will cooperate in registering and updating inventory.
- Required legal approvals will be secured before launch.
- The app may require internet access for live updates.

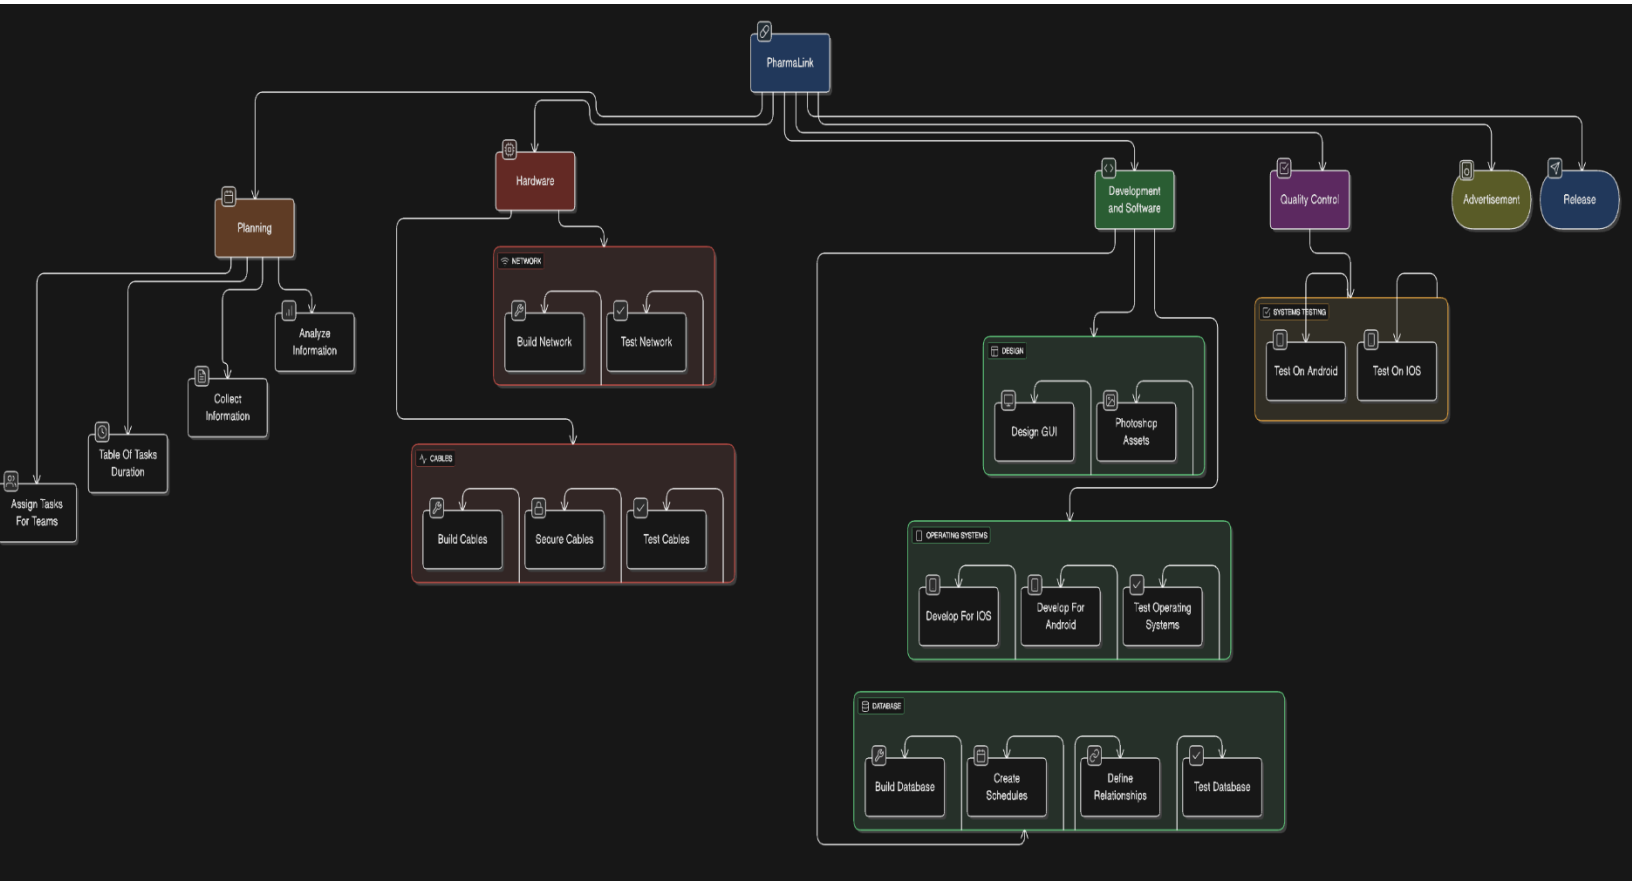
PharmaLink
Planning
Hardware
Development and Software
Quality Control
Advertisement
Release
Assign Tasks For Teams
Table Of Tasks Duration
Collect Information
Analyze Information
NETWORK
Build Network
Test Network
CABLES
Build Cables
Secure Cables
Test Cables
DESIGN
Design GUI
Photoshop Assets
OPERATING SYSTEMS
Develop For IOS
Develop For Android
Test Operating Systems
DATABASE
Build Database
Create Schedules
Define Relationships
Test Database
SYSTEMS TESTING
Test On Android
Test On IOS

Code	Description	Persons	Resources	Cost (EGP)	Timeline
1	Planning		6R	40,000	15/10 → 31/10
1.1	Assign Tasks & Duration Table	Manager, Team Members	2R	20,000	15/10 → 20/10
1.2	Collect Information	Mohamed Abdelmoez, Youssef	2R	10,000	20/10 → 25/10
1.3	Analysis Information	Mohamed Abdelmoez, Mena	2R	10,000	25/10 → 31/10
2	Hardware, Network & Licenses		5 Laptops, Server, 5 Mobiles, IDE, APIs, Router, Switches, Cables, 6R	100,000	01/11 → 31/01
2.1	Buy Hardware	Mohamed Alhaitham	1R	60,000	01/11→02/11
2.2	Build Cables	Mena	1R	15,000	03/11 → 15/12
2.3	Test Cables & Security	Yousab	1R	5,000	15/12 → 18/12
2.4	Build Network	Mohamed Abdelmoez	1R	15,000	18/12 → 05/01
2.5	Test Network	Yousef, Mena	2R	5,000	05/01 → 10/01
3	Development		7R	200,000	01/11 → 20/02
3.1	UI/UX Design	Mena	1R	20,000	01/11 → 10/11
3.2	Backend Design	Mohamed Alhaitham	1R	20,000	10/11 → 20/11
3.3	Mobile App (Flutter)	Youssef, Mena	2R	90,000	21/11 → 31/12
3.4	Backend Server	Mohamed Alhaitham	1R	45,000	01/01 → 15/01
3.5	Real-time Inventory	Mohamed Abdelmoez, Yousab	2R	25,000	16/01 → 20/02
4	Quality Control	Yousab, Mena	2R	45,000	21/02→ 14/03
5	Release	Mohamed Abdelmoez, Mohamed Alhaitham	2R	25,000	15/03→22/03
6	Advertisement & Marketing	Yousab	1R	40,000	23/03 → 01/04

Task	Mohamed Abdelmoez	Youssef	Mena	Yousab	Mohamed Alhaitham
Assign Tasks for Teams & Table of Tasks Duration	R	S			S
Collect Information	S	R			S
Analysis Information		S	R	S	
Cables	S		S	R	
Network		S		S	R
Database	S		R		S
Design		S		R	S
Operating System	S		S	S	R
Quality Control	R	S			S
Release	S	R		S	
Advertisements				R	S

A	Planning		2W
B	Hardware, Network & Licenses	A	13W
C	Development	A	16W
D	Quality Control	B,C	3W
E	Release	D	1W
F	Advertisement & Marketing	E	1W

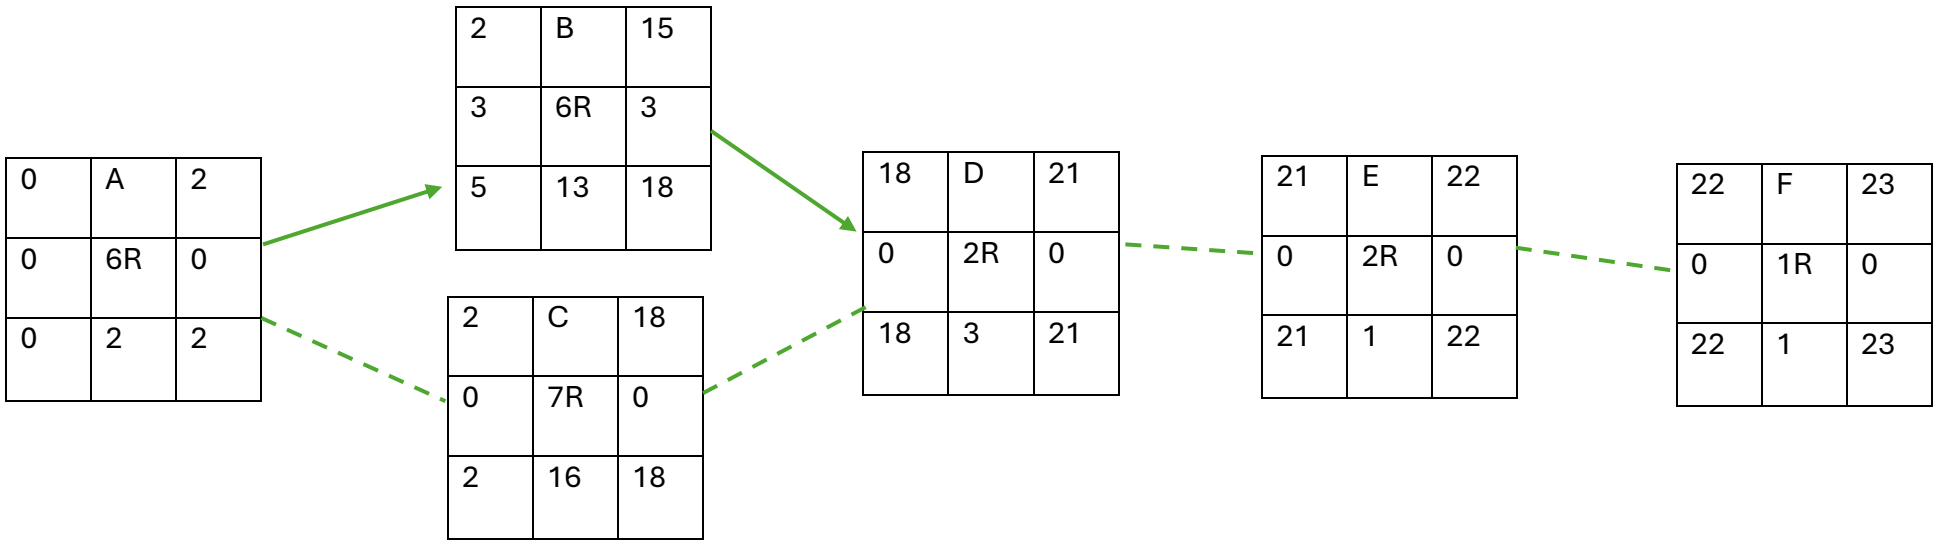

RESUORCE ALLOCATION

ID	RES	DUR	ES	LF	SL	0	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23
A	6	2	0	2	0	6	6																						
B	6	13	2	18	3			6	6	6	6	6	6	6	6	6	6	6	6	6	6								
C	7	16	2	18	0			7	7	7	7	7	7	7	7	7	7	7	7	7	7	7	7	7					
D	2	3	18	21	0																				2	2	2		
E	2	1	21	22	0																							2	
F	1	1	22	23	0																								1
TOTAL						6	6	13	13	13	13	13	13	13	13	13	13	13	13	13	13	7	7	7	2	2	2	2	1
AVAILABLE						13	13	13	13	13	13	13	13	13	13	13	13	13	13	13	13	13	13	13	13	13	13	13	13

Risk management:

Risk: Scope Creep (Client adds more work):

Solution:

- Create clear scope document
- Change requests must be approved
- Set limits on changes

Risk: Technical Issues (software/hardware fails)

Solution:

- Test early and frequently
- Keep backup equipment
- Use stable, proven technology
- Have an IT support plan

Risk: Schedule Delays

Solution:

- Use strong planning (Gantt chart, milestones)
- Prioritize critical tasks first
- Monitor progress daily/weekly

Risk: Poor Communication:

Solution:

- Hold weekly team meetings
- Use a shared platform (Teams, Slack, WhatsApp group)
- Write clear instructions
- Document decisions

Risk: Quality Problems:

Solution:

- Create quality standards
- Test early, test often
- Have acceptance criteria

Risk: Data Loss:

Solution:

- Backup data daily
- Store copies in cloud (Google Drive, OneDrive)
- Use antivirus and security tools
- Limit access to important files

($000) Week

ID	TASK	DUR(W)	BUDGET	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23
1	**Planning**	2	40	20	20																					
2	**Hardware, Network & Licenses**	13	100			10	10	10	10	10	5	5	5	10	5	5	10	5								
3	**Development**	16	200			12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	20					
4	**Quality Control**	3	45																			15	15	15		
5	**Release**	1	25																						25	
6	**Advertisement & Marketing**	1	40																							40
Week total			450	20	20	22	22	22	22	22	17	17	17	22	17	17	22	17	12	12	20	15	15	15	25	40
Cumulative				20	40	62	84	106	128	150	167	184	201	223	240	257	279	296	308	320	340	355	370	385	410	450

Cumulative Baseline Budget(PV)

